Permeable Paver Projects: Contractor Estimate Checklist

You will be required to provide a copy of the project proposal/estimate provided by your contractor as part of your application.


Permeable Pavement Minimum Requirements:

- ☐ Installed according to MDE Ch.5 Guidelines
- ☐ Minimum paver area of 100 square feet
- ☐ Contractor must have attended a PICP (Permeable Interlocking Concrete Pavers) training course through ICPI (Interlocking Concrete Pavement Institute) or have a portfolio showing at least five permeable projects and references.
- ☐ Cannot treat additional impervious surfaces (only footprint of the paver area)
- ☐ Only costs associated with the permeable portion of the project will be considered for reimbursement.

For each Permeable Paver project please ensure the contractor estimate includes the following:

- ☐ **Size** of Permeable Pavement (minimum is 100 ft2):
- ☐ Are you **removing an impervious surface** prior to installation?
  - If yes, what is the size of impervious removal?
- ☐ **Cost** of Permeable Pavement:
- ☐ Was an infiltration test conducted or is one planned?
  - If so, what was the rate?
- ☐ **Location** where the pavers will be installed should be clearly shown or described. (example: Driveway footprint, or a picture of the location)
- ☐ Does your contractor estimate include a **profile view** showing both depth of the practice and gravel media?

Example:

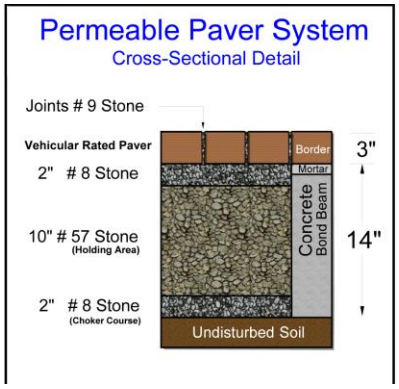

CleanScapes Program
https://www.cleanwaterhoward.com/what-your-role/residential-properties/cleanscapes
